



**MHHS
PROGRAMME**
Industry-led, Elexon facilitated

Migration and Cutover Advisory Group (MCAG) #22 – 24 February 2026

Version 1.0

MHHS-DEL4420

Agenda


#	Item	Objective	Type	Lead	Time	Page
1	Welcome	Chair welcome	Information	Chair		
2	Headline Report and Actions	Approval of Headline Report of previous meeting and review of outstanding actions	Decision	Secretariat	14:00-14:05 5 mins	3
3	Migration Execution	Update on the progress of Migration Execution	Information	Programme (Warren Fulton)	14:05-14:15 10 mins	5
4	Participant-Driven Migration Dependencies	Update on Migration dependencies on industry participants	Information	Programme (Warren Fulton)	14:15-14:25 10 mins	7
5	Migration Exclusion List	Update on the Migration Exclusion and Remediation list	Information	Programme (Joe Grisley)	14:25-14:35 10 mins	11
6	MWG Update	Update on MWG activities and progress	Information	Programme (Joe Grisley)	14:35-14:45 10 mins	18
7	STEG Update	Update on STEG activities and progress	Information	Programme (Ian Smith)	14:45-14:55 10 mins	21
8	Programme Milestones related to MCAG	Overview of upcoming Programme Milestones related to MCAG and any milestone changes for approval	Information	Programme (PMO)	14:55-15:00 5 mins	23
9	Top Programme Risks related to MCAG	Overview of Programme Risks related to MCAG	Information	Programme (PMO)	15:00-15:05 5 mins	25
10	Programme Updates	Provide updates from L2/3 governance groups and wider Programme activity	Information	Programme (PMO)	15:05-15:05 0 mins	27
11	Summary and Next Steps	Summarise actions/decisions and look ahead to the next MCAG	Information	Chair and Secretariat	15:05-15:10 5 mins	30

Headline Report and Actions

DECISION: Approval of Headline Report of previous meeting and review of outstanding actions

Secretariat

5 mins



Actions Review

- 1. Approval of Headline Reports from MCAG held [12 February 2026](#)
- 2. **Review outstanding actions** (actions will be discussed by exception. Please review the action updates ahead of the meeting)


Ref	Action	Owner	Due	Latest Update
-----	--------	-------	-----	---------------

Migration Execution

INFORMATION: Update on the progress of Migration Execution


Programme (Warren Fulton)

10 mins



Migration Execution

1. Six suppliers are actively migrating.
2. As of 15 Feb 2026, a total of 2.7 million migrations have been completed against a planned 2.9 million. Completions are approximately 200,000 below target following a pause in migration activities due to incident INC0131738, which delayed 350,000 migrations. Recovery is underway, although it is taking slightly longer than anticipated, and progress is expected to be back on track by 1 Mar 2026.
3. Total exceptions remain low. Exception trends and preventative actions are reviewed at MWG.
4. There have been no LDSO, DCC, or DIP threshold breaches.
5. Migrating suppliers are fully compliant with their baseline plans.

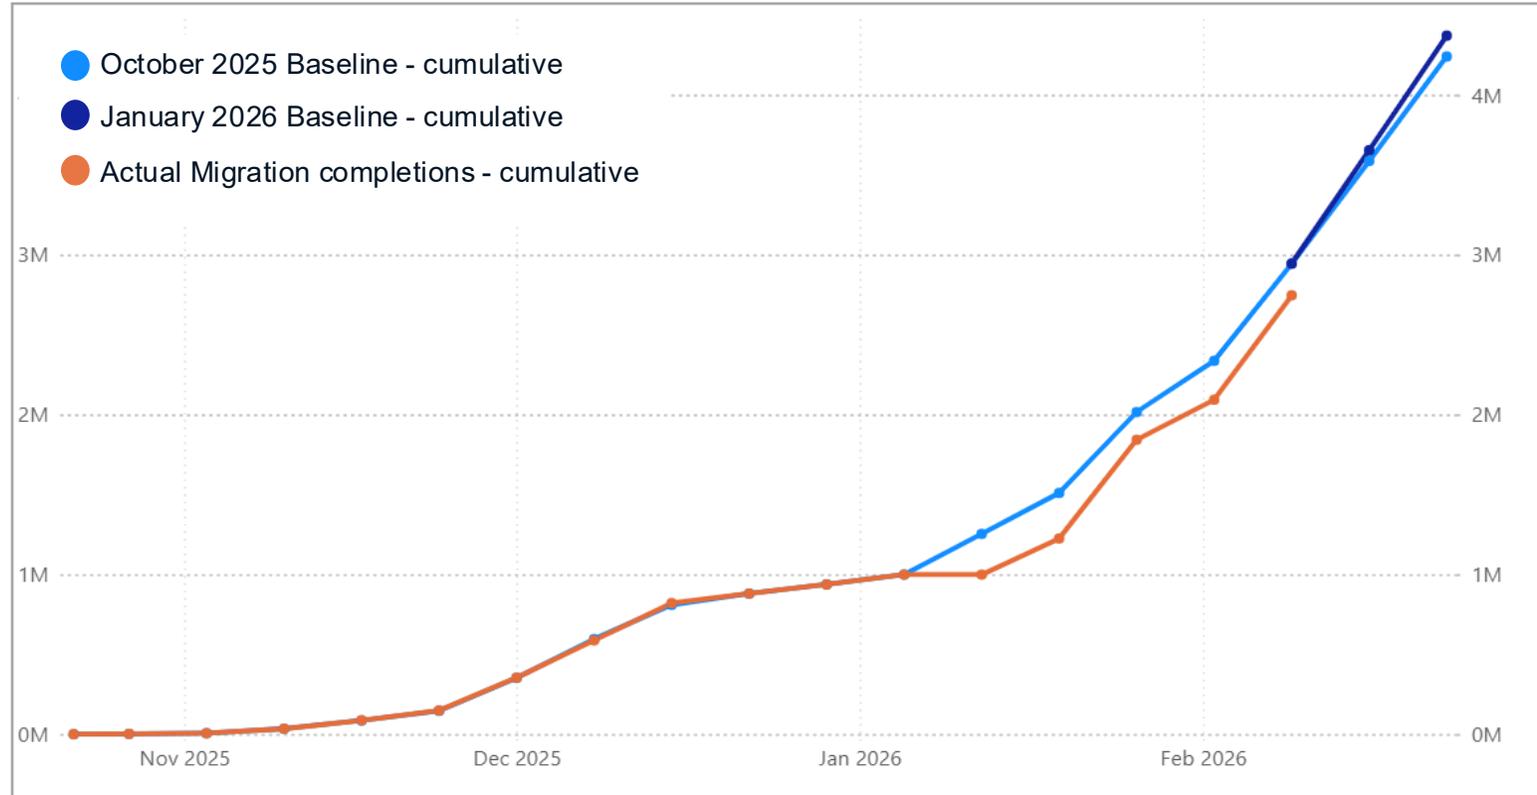


Participant-Driven Migration Dependencies

INFORMATION: Update on Migration dependencies on industry participants

Programme (Warren Fulton)

10 mins



Core Migration Dependencies (1)

ID	Title	Description	Previous RAG	Current RAG	Forecast RAG	Commentary
D351	Early Life Support	There is a dependency on Early Life Support completing within the assumed 3-month period and the ramp-up not being delayed	A	C	C	ELS exit was approved by MCAG on 12 Feb 2026
D359	Supplier Migration performance	There is a dependency on Suppliers adhering to the Migration Framework and Migration Plan	G	G	G	Migrating Suppliers are compliant with the Migration Framework and Plan
D419	Suppliers resolving problematic MPANs	There is a dependency on Suppliers to proactively identify, assess and resolve potential problem MPANs before M15 (noting D418 on Code Bodies)	G	G	G	There are no known issues affecting Sprint 1 progress. The Exclusion List PPIR has been issued and the findings will be published in April 2026
D220	Supplier and Agent qualification	There is a dependency on Suppliers and Agents to complete Qualification in alignment with their planned migration start dates.	G	G	G	There are no known Supplier or Agent Qualification issues materially affecting the planned migration start dates.
D340	Qualification Testing performance	There is a dependency on Elexon's Qualification Testing capability for Participants to qualify in line with their planned Migration Start date	G	G	G	There are no known Qualification Testing performance issues affecting planned migration start dates.
D361	Agent dependencies	There is a dependency on Suppliers managing their agent dependencies to meet the agreed Migration Schedule	G	G	G	There are no known Agent Qualification issues affecting Supplier planned migration start dates.
D341	BSC Qualification Governance performance	There is a dependency on the BSC PAB governance process for Participants to qualify in line with their planned Migration Start date	G	G	G	There are no known BSC Qualification Governance performance issues affecting planned migration start dates.
D415	REC Qualification Governance performance	There is a dependency on the REC Code Manager governance process for Participants to qualify in line with their planned Migration Start date	G	G	G	There are no known REC Qualification Testing performance issues affecting planned migration start dates.

Core Migration Dependencies (2)

ID	Title	Description	Previous RAG	Current RAG	Forecast RAG	Commentary
D221	Service Activation performance	There is a dependency on Elexon's Service Activation capability for Participants to start migration in line with their planned Migration Start	G	G	G	Discussions are in progress to increase the ISD publication frequency during peak Qualification periods.
D342	DIP Onboarding performance	There is a dependency on Elexon's DIP onboarding capability for Participants to start migration in line with their planned Migration Start	G	G	G	There are no DIP onboarding issues affecting planned migration start dates. Several areas for improvement have been identified for later Sprints. Proposed Readiness Assessment 7 from PPIR results will provide confidence on future capability and capacity.
D417	Service Management performance	There is a dependency on Elexon Service Management adhering to SLAs for Participants to migration in line with their baselined Migration plans	G	G	G	There are no known issues affecting Sprint 1 progress.
D416	DIP migration performance	There is a dependency on Elexon DIP performance adhering to requirements and SLAs for Participants to migration in line with their baselined Migration plans	G	G	G	There are no known issues affecting Sprint 1 progress.
D343	Settlement performance	There is a dependency on the new MHHS settlement processes working as expected and not causing any reason for Migrations to be stopped	G	G	G	There are no known issues affecting Sprint 1 progress.
D373	LDSO migration performance	There is a dependency on LDSO's performing as per the agreed Migration Thresholds for Participants to migration in line with their baselined Migration plans	G	A	A	There have been several instances where LDSOs have experienced system issues, resulting in delays in processing IF-31s and issuing subsequent messages. In some cases, IF-32 responses were issued after the 5:00 pm SLA defined in the Migration Framework. However, due to the migration offset, these delays have not impacted migration completions, as messages were ultimately processed and sent prior to the effective-from date. LDSOs have not consistently raised these issues with the MCC, meaning Suppliers and the MCC were not always informed. This has led to uncertainty regarding the progress of migrations. LDSOs are reminded of their obligations under the Migration Framework and are expected to notify the MCC should any unplanned issues occur. The MCC will continue to monitor the associated risk.

Core Migration Dependencies (3)


ID	Title	Description	Previous RAG	Current RAG	Forecast RAG	Commentary
D369	DCC migration performance	There is a dependency on DCC performing as per the agreed Migration Thresholds for Participants to migration in line with their baselined Migration plans	G	G	G	DCC processed migrations in accordance with the Migration Design and Migration Threshold obligations
D352	Industry change – Preventing Migration	There is a dependency on Code Bodies to ensure that industry change does not impede Participants from fulfilling their MHHS obligations and/or delay migration	G	G	G	There are no known Industry Changes affecting Participant Migration plans or performance.
D418	Industry change – Enabling Migration	There is a dependency on Code Bodies to implement changes to allow Suppliers to migrate MPANs on the Migration Exclusion list. (Noting the volume of affected MPANs is relatively low)	G	G	G	There are no known issues affecting Sprint 1 progress.

Migration Exclusion List

INFORMATION: Update on the Migration Exclusion and Remediation list

Programme (Joe Grisley)

10 mins



Migration Troublesome MPANs PPIR

PPIR Timelines remain on track with PPIR and Guidance Document due to be published on the 16th February.

- The PPIR was published to Suppliers and Agents, along with guidance documentation on the **16th February 2026**.
- Suppliers and Agents will be provided with a 4-week window to complete the PPIR. The PPIR Deadline is the **13th March 2026**.
- Following the publication of the PPIR, weekly drop-in sessions will be held with parties to support the completion of the PPIR.
 - Drop-in Session 1 – 19th February 2026
 - Drop-in Session 2 – 26th February 2026
 - Drop-in Session 1 – 5th March 2026
 - Drop-in Session 1 – 12th March 2026

This PPIR aims to:

- Ask for Suppliers to identify the volume of MPANs relating to each Exclusion and Remediation List item within their portfolio.
- Ask for Suppliers to provide a resolution plan for how they aim to resolve their volume of Exclusion / Remediation MPANs in line with their migration plan.
- Ask for Suppliers to share the volume of Complex sites, shared SVA Metering Systems and private network arrangements they have within their portfolio.
- Ask for Suppliers to share the volume of MPANs with a Trading Status of X and they plan to deregister or migrate these MPANs.
- Ask Agents to share the volume of Complex sites, shared SVA Metering Systems and private network arrangements they have within their portfolio and the Suppliers involved.

Note - Due to the developing position on the SMETS 2 Incorrect Number of Dials issue, the Migration Team are not planning on including this item within the PPIR until code body activities have progressed further. This is to avoid asking participants the wrong questions.

Migration Exclusions – Code Changes and Constraints

BSC					
Exclusion and Remediation Item	Code Change	CP	Target Implementation date	Progress update	RAG
CSS Registration ID	BSC Change required to make conditionally mandatory CSS Reg ID field mandatory	TBC	TBC	CP yet to be raised. This CP however is a lower priority change to align design documentation to behaviour witnessed in production.	Yellow
Traditional meters installed on CT connection types	BSC Change required to permit Traditional CT meters as a valid configuration	CP1628	25-June-26	CP1628 is currently being out for consultation with decision scheduled for March.	Green
Related MPANs with different meter types					
SMETS 2 Incorrect Number of Digits	BSC Change required to change SMRS Validation rules	CP1622	25-June-26	SVG have decided to pause CP1622 in its current form while cross-code activities bring together BSC, REC, the MHHS Programme and impacted Market Participants to confirm an enduring approach. Initial meeting held with industry. Code Body guidance provided states that this issue is not migration impacting. Cross-code activities are continuing to identify resolution.	Green

REC					
Exclusion and Remediation Item	Code Change	CP	Target Implementation date	Progress update	RAG
CSS Registration ID	Back population of CSS Reg ID to enable Supplier to source it from EES	N/A	June	REC have established issue group I0296 – Link to issue group can be found here REC looking to provide Suppliers with CSS Reg ID reports to enable back population activity. Aiming for a no later than date of June.	Green
SMETS 2 Incorrect Number of Digits	REC change to D0312	R0300	25-June-26	SVG have decided to pause CP1622 in its current form while cross-code activities bring together BSC, REC, the MHHS Programme and impacted Market Participants to confirm an enduring approach. Initial meeting held with industry. Code Body guidance provided states that this issue is not migration impacting. Cross-code activities are continuing to identify resolution.	Green

DCC				
Exclusion and Remediation Item	Target Completion date	Progress update	RAG	
SMETS 1 FOC incorrectly configured	30/01/26	DCC have now provided reporting to all impacted Suppliers (51). Suppliers now have what they need to progress the SMETS 1 FOC issue.	Blue	

Migration Exclusion List

Issue Type	MPAN Volume	Description	Migration Status	Migration Commentary	Remedial Action	Industry Owner (Responsible Party)	Responsible Code (Change)	Current Status	Target Date	RAID Item	Code Change
Traditional meters installed on CT connection types	6,000	The design does not support traditional meters installed on CT connections. Migration should not be attempted for these specific MPANs until this issue is resolved. The traditional meter should be exchanged for an advanced meter prior to migration; or, if the meter cannot be exchanged the MPAN should not be migrated until a BSC change to support this scenario is implemented.	Blocked	1.b Pot Unmigratable without change due to design. Only Blocked if you intend to migrate the traditional CT meter	1a. Supplier and MOP identify MPANs with a traditional meter on a CT connection and replace that meter for an advanced meter; or	1a. Supplier	BSC	In Progress		i217	YES
					1b. Supplier and MOP follow process set out within BSC change xxxx (when implemented); or	1b. Supplier & MOP	BSC	Blocked	Jun-26		
					1c. Supplier and MOP determine that connection is not CT and request LDSO amend the connection type to W	1c. Supplier & MOP & LDSO	BSC	In Progress			
					2. Following 1a or b MOP sends correct D0312 to MPRS	2. Supplier & MOP	REC	In Progress			
					3. Following 1c LDSO sends DB02 to MPRS, MPRS will re-evaluate the market segment from advanced to smart	3. LDSO	BSC	In Progress			
					4. Supplier can migrate the MPAN once correction made.	4. Supplier		Partially Blocked	Jun-26		
Related MPANs with different meter types	8,400	Related MPANs with different meter groups which create different market segments (e.g. smart and advanced) will cause exceptions if the MPAN migration is attempted. The design doesn't support related MPANs with two different market segments.	Partially Blocked	Trad CT scenario of related are currently UNMIGRATABLE in current stage blocked until code change implemented. Remaining scenarios defer until cleansing activity has been completed	1. Supplier unrelates MPANs if relationship not required for billing purposes, by sending the D0386; or	1. Supplier	REC	In Progress		i234	YES
					2. If required for billing purposes; Supplier must not migrate until:	2. Supplier	REC	In Progress			
					3. Meter exchanges are completed to align the meter group across all MPANs; or	3. Supplier	REC	In Progress			
					4. Industry change to MHHS design implemented to support different meter groups.	4. Code Body	BSC	Blocked	Jun-26		
					5. Supplier can migrate MPAN following step 1, 3 or 4.	5. Supplier		Partially Blocked	Jun-26		

Migration Remediation List (1 of 3)

Issue Type	MPAN Volume	Description	Migration Status	Migration Commentary	Remedial Action	Industry Owner (Responsible Party)	Responsible Code (Change)	Current Status	Target Date	RAID Item	Code Change
CHECK meter types in MPRS	50	MOPs should not send CHECK meters within a D0312 to MPRS. CHECK meters are not supported within the design and will cause migrations to fail if attempted. CHECK meters will need to be removed via the D0312 prior to that MPAN being migrated.	Defer	Unmigratable in current stage. Defer until cleansing activity has been completed	1. MOP removes CHECK meter from MPRS via D0312.	1. Supplier	REC	In Progress		i230	NO
					2. Supplier can initiate migration for MPAN once correction made	2. Supplier		In Progress			
Smart meters and CT connection types	600	It is not possible for smart meters to be installed on CT connection types, so a clear data quality issue exists. These MPANs will not migrate successfully and will cause exceptions if migration is attempted before they are fixed.	Defer	Unmigratable in current stage. Defer until cleansing activity has been completed	1. Supplier checks that smart meter installation is valid, if valid 2, if not valid 3	1. Supplier	REC	In Progress		i231	NO
					2. Supplier raises a request with the LDSO to correct connection type to WC.	2. Supplier	BSC	In Progress			
					3. MOP correct meter type to valid value which is supported by CT connection type and send new D0312.	3. Supplier	REC	In Progress			
					4. Supplier can initiate migration for MPAN once correction made	4. Supplier		In Progress			
Linked import and export MPANs with different connection types	2,000	The design doesn't support linked MPANs within different market segments. Exceptions will be created preventing the successful migration of an MPAN if attempted. The data misalignment should be resolved if the linkage is correct, or the linkage should be removed if the data for the respective MPANs is correct.	Defer	Unmigratable in current stage. Defer until cleansing activity has been completed	1. LDSO check the connection types and amends if incorrect or de-links the MPANs if correct.	1. LDSO	BSC	In Progress		i232	NO
					2. Supplier can then migrate the MPAN	2. Supplier	BSC	In Progress			
Linked import and export MPANs with different meter types	330	The design doesn't support linked MPANs within different market segments. Exceptions will be created preventing the successful migration of an MPAN if attempted. The data misalignment should be resolved if the linkage is correct, or the linkage should be removed if the data for the respective MPANs is correct.	Defer	Unmigratable in current stage. Defer until cleansing activity has been completed	1. Supplier investigates the linked MPANs and changes the meter type if incorrect, if the other MPAN is with another Supplier and that Suppliers meter type is incorrect then they should raise an SDEP to that Supplier to update; or	1. Supplier	BSC	In Progress		i218	NO
					2. Supplier believes the MPANs should not be linked and requests, via SDEP, that the LDSO de-links them.	2. Supplier	BSC	In Progress			
					3. Following 1 or 2 completion the MPAN can be migrated.	3. Supplier	BSC	In Progress			

Migration Remediation List (2 of 3)

Issue Type	MPAN Volume	Description	Migration Status	Migration Commentary	Remedial Action	Industry Owner (Responsible Party)	Responsible Code (Change)	Current Status	Target Date	RAID Item	Code Change
Related MPANs with different connection types	300	Related MPANs with different connection types will cause exceptions if the MPAN migration is attempted. The design doesn't support related MPANs with two different market segments.	Defer	Unmigratable in current stage. Defer until cleansing activity has been completed	1. LDSO investigates exceptions and corrects connection type if incorrect, or	1. LDSO	BSC	In Progress		i233	NO
					2. LDSO raises SDEP and instructs the Supplier to unrelate	2. LDSO	REC	In Progress			
					3. Supplier unrelates if instructed to by LDSO, by sending the D0386	3. Supplier	REC	In Progress			
					4. Supplier can migrate MPAN following step 1 or step 3.	4. Supplier		In Progress			
NHH unmetered MPAN	2,500	NHH MPANs cannot be migrated to MHHS, only HH MPANs can be migrated.	Defer	Unmigratable in current stage. Defer until P434 Obligation has completed	1. Change measurement class of MPAN from NHH to HH.	1. Supplier	BSC	In Progress		R897	NO
					2. De-register any secondary unmetered MPANs	2. Supplier		In Progress			
					3. Migrate MPAN	2. Supplier	BSC	In Progress			
Domestic Unmetered MPANs	50	~50 MPANs impacted Domestic Unmetered MPANs cannot be migrated to MHHS.	Defer	Unmigratable in current stage. Defer until cleansing activity has been completed	1. Change DPI to Non-Domestic as per process set out in REC	1. Supplier	REC	In Progress		i224	NO
					2. Migrate MPAN	2. Supplier		In Progress			
CSS Registration ID	TBC	If Registration ID is not populated with the IF-031, the message will be rejected by the Registration Service. There is a potential issue that suppliers do not have complete Registration ID records. A conflict currently exists between the Registration Service functionality and the baselined design / codes.	Defer	Unmigratable in current stage. Defer until cleansing activity has been completed	1. Supplier to populate CSS RegistrationID	1. Supplier	REC	In Progress		R1198	YES
					2. Migrate MPAN	2. Supplier		In Progress			

Migration Remediation List (3 of 3)

Issue Type	MPAN Volume	Description	Migration Status	Migration Commentary	Remedial Action	Industry Owner (Responsible Party)	Responsible Code (Change)	Current Status	Target Date	RAID Item	Code Change
SMETS 1 FOC incorrectly configured	c. 2,300,000	SMETS1 meters impacted by the incorrect recording of HH interval data	Defer	Possible to migrated however the HH settlement data may be incorrect	1. DCC to implement a fix to allow the reconfiguring of the SMETS1 Meters to resolve the identified issue to ensure all consumption data retrieved from these meters is accurate.	1. DCC	SEC	DONE	12-Jan-26	R1201	NO
					2. Suppliers to work with MOPs to resolve non communicated MPANs and to then Migrate once fix has been applied	2. Supplier		In Progress			
SMETS 2 Incorrect Number of Digits	250,000	Circa. 250,000 MPANs have a "number of register digits" value that is different to the value populated within MPRS. Currently the D0150 will contain the correct value but this information will not be present once an MPAN is migrated as the D0150 is no longer used.	Defer	Possible to Migrated, however could impact Settlement. Following BSC and REC change	1. BSC change required to change MPRS to be able to accept the correct "number of register digits" value via the D0312 data flow.	1. BSC & LDSOs	BSC	In Progress	25-Jun-26	i211	YES
					2. MOPs identify meters within their portfolio which will have an incorrect "number of register digits" held within MPRS (this can be achieved by comparing the value they hold to the previous MPRS validation rules).	2. Supplier	REC	Defer			
					3. MOPs to send corrected value to MPRS via the D0312 data flow.	3. Supplier	REC	Defer			
					4. Supplier can migrate the MPAN once correction made.	4. Supplier		Defer			
Missing Meter Data (Energised) within MPRS	17,000	MPANs which do not have meter data populated within MPRS at the point of market segment population in September 2025 will be set to a market segment of advanced. In many instances a smart meter is installed on this site, unless the correct meter data is populated by the MOP in MPRS only advanced agents could be appointed when the MPAN is migrated. The Supplier should not attempt migration until the correct data is populated via the D0312 flow.	Defer	Possible to migrate, however it would have to be migrated within the Advanced segment. If this is incorrect, Supplier would be required to complete a change of segment	1. Supplier and MOP identify MPANs with missing meter data within MPRS. Utilising the REC performance assurance reporting and EES reporting.	1. Supplier	REC	In Progress		i145	NO
					2. MOP sends correct D0312 to MPRS.	2. Supplier	REC	In Progress			
					3. If the D0312 meter type is smart or traditional MPRS will re-evaluate the market segment from advanced to smart.	3. LDSO (automated process)	REC	In Progress			
					4. Supplier can migrate the MPAN once correction made.	4. Supplier		In Progress			
Linked & Related Import and Export MPANs with Export MPAN Missing meter data	TBC	MPANs which do not have meter data populated within MPRS at the point of market segment population in September 2025 will be set to a market segment of advanced. In the instance of linked or related Import and Export MPANs where the Export MPAN is missing meter data, the Export MPAN will default to the Advanced segment. This will result in the Import MPAN also defaulting to advanced even if it is correctly set to Smart.	Defer	Possible to migrate, however should the segment incorrectly default it would cause significant operational intervention to resolve within the MHHS arrange	1. Solution to be discussed at MHHS Expert Group	1. Supplier	BSC	In Progress			TBC


* Linked & Related Import and Export remains Amber due to solution discussions being ongoing at BSC Expert Group

MWG Update

INFORMATION: Update on MWG activities and progress

Programme (Joe Grisley)

10 mins



MWG focus

At MWG 48, the Migration team took industry through the Migration Execution summary, as well as taking industry through the output of Sprint 1 Planning and the Migration Exclusions.

The central lessons learnt repository was also introduced. This was established to capture lessons across the end-to-end participant journey. The Repository enables the programme and industry to share lessons learned, strengthen participant readiness, and improve confidence in meeting MHHS milestones. It forms a key part of creating a consistent, structured learning loop across MHHS delivery. Please find a link to the lessons learnt repository [here](#).

MWG actions

There are 2 open actions with MWG.

- 1 item relates to Mod P487 which is ongoing
- 1 item relates to the action on the DCC to provide SMETS 1 FOC reporting which has now been completed – as such this will be recommended to close at the next MWG.

MWG backlog

There are 3 items remaining on the MWG Backlog which will continue to be progressed:

- 2 are standing items that relate to ongoing updates and maintenance to the Migration Framework
- 1 item relates to SoLR processes that are ongoing

MWG Backlog - Outstanding Items and Activities Scheduled for Completion with MWG


ID	Name	Description	Update	Status
7	Framework Parameter adjustments	Potential changes to Parameters – based on findings from Supplier Submission 2	Standing item	Open
14	DIN-1189 - Thresholds Document update – CSS and DSP messages (item raised by a Participant)	Update MHHS Migration Thresholds Document - tables outlining the Migration Messages received and sent by the CSS and DSP.	The redlining has been completed and will be progressed along with other changes to the Migration Framework following the end of ELS	Open
15	Migration Capacity during SoLR	Discussion required to work through scenarios	Ongoing, discussion underway with Ofgem	Open

STEG Update

INFORMATION: Update on STEG activities and progress

Programme (Ian Smith)

10 mins



STEG focus

- The first STEG session took place on 6th February 2026
- Focus for the initial session:
 - Recap of Transition Design baselined in 2023
 - Overview of Governance Choreography Proposal
 - Initial Plan on a Page
 - Initial proposal for Settlement Metric monitoring from Performance Assurance.

Key Next Steps

- There was a very constructive discussion around monitoring proposals. Points and suggestions from this discussion are being developed for discussion in the next session.
- The group also expressed a wish for greater clarity on planning with particular regard to dependencies around decision points and subsequent updates to the settlement calendar. Further detail will be provided at the next session.


Next STEG session to be held on 26th February

Programme Milestones related to MCAG

INFORMATION: Overview of upcoming Programme Milestones related to MCAG and any milestone changes for approval

Programme (PMO)

5 mins



Look Ahead – Key Milestones Status on 17 February 2026

To align to weekly reporting, the previous, current and forecast RAGs reflect milestone status from last week, this week and next week, respectively.


Milestone	Milestone Title	Forum	Baseline Date	Forecast Date	Responsible	Previous RAG	Current RAG	Forecast RAG	Commentary
T3-MI-0500	M16 methodology approved	MCAG (Transition)	31 July 2026	31 July 2026	SI Transition				11/02/26 - M16 Plan under development and will be included in the Programme Plan soon.
T2-RA-0600	Readiness Assessment 7 - Migration Checkpoint - Completed (incl. Readiness Assessment Report approval)	PSG	01 April 2026	01 April 2026	CPT				11/02/26 - Readiness Assessment 7 Checkpoint updated to reflect the approach agreed with PSG
T1-MI-5000	All suppliers must be able to access MPANs under the new TOM (M14)	PSG	28 October 2026	28 October 2026	CPT				13/02/26 - Activity On-track
T2-MI-8500	Non-SIT Participants Migration Start	MCAG (Migration)	15 May 2026	15 May 2026	SI Migration				13/02/26 - Activity On-track
T2-MR-0200	M14 milestone checkpoint - date approval	PSG	06 August 2026	06 August 2026	CPT				13/02/26 - Activity On-track
T2-RA-0600	Readiness Assessment 7 - Migration Checkpoint - Completed (incl. Readiness Assessment Report approval)	PSG	19 March 2026	31 October 2022	CPT				13/02/26 - Activity On-track
T2-RA-0700	Readiness Assessment 8 - Ready to Accept New MPANs - Completed (incl. Readiness Assessment Report approval)	PSG	13 October 2026	13 October 2026	CPT				13/02/26 - Activity On-track

Top Programme Risks related to MCAG

INFORMATION: Update on the top Programme risks related to MCAG


Programme (PMO)

5 mins



Top Programme Risks related to MCAG

This risk assessment is based on no incentives being in place - and it will be reviewed should P487 be approved. Post ELS, all risks will be re-reviewed and updated in line with exit position.

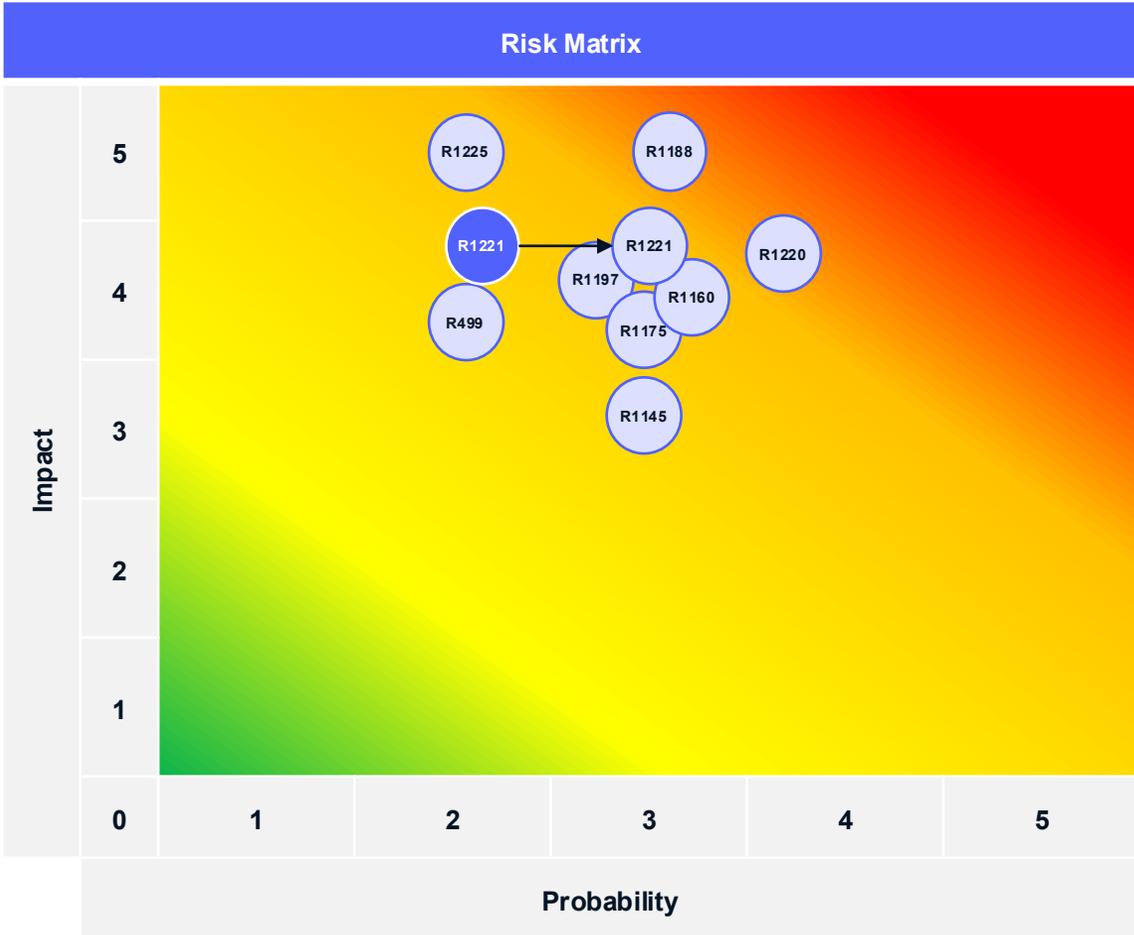

Risk ID	Risk	Mitigation	Contingency Plan	Previous Score	Current Score
R1188	There is a risk that issues between the registration service and suppliers may not be responded to and/or resolved in a 'timely manner' during Migration, as set out in BSCP706.	<ul style="list-style-type: none"> Issue with D0209s has shown that this risk has materialized This is related to ELS recommendation 4, on cross party service desks that was shared at TORWG on 04-Feb (are process controls/SLAs required in the code). MCC may need some controls around LDSOs releases if cross party service desk issue is not progressed. MHSP are reliant on seeing progress from Elexon on recommendation list above. 		20	20
R1220	There is a risk that the Service Delivery function, including Service Management, Performance Assurance, Market Design, OSMs, is unable to scale or operate at sufficient maturity to manage the increased volume and complexity of issues during peak migration periods impacting achievement of M15	<ul style="list-style-type: none"> Elexon to ensure resourcing in place to support additional participants as they begin migration and ensure knowledge base is kept up to date through early weeks of migration and applying any lessons learnt. Programme continues to have concerns on how triage and incident management are working currently. Elexon are reviewing Service Delivery in response to the ELS recommendations 		19	19
R1160	There is a risk that the DIP Manager team do not have the capacity to deal with the volume of PPs going through onboarding	<ul style="list-style-type: none"> PPIR responses will provide visibility of expected PP onboarding volumes and timelines, enabling early identification and mitigation of any peak onboarding demand within a SWD period 		16	16
R1175	There is a risk that the lack of QT progress could delay the completion of QT for PPs impacting Migration timelines	<ul style="list-style-type: none"> Proactive monitoring and assurance of QT testing progress and non-SIT PP tracker Further highlighting to PPs what date they will need to complete QT in order to hit Migration start dates, as per R1215. Wave 1 complete and wave 2&3 tracking ahead of schedule 	<ul style="list-style-type: none"> Delayed PPs would be in breach of license conditions 	14	14
R1197	There is a risk that Suppliers may have data quality issues or other initial business reasons why MPANs are not deemed to be in a fit state for migration and therefore migration to the new MHHS settlement arrangement is not initiated.	<ul style="list-style-type: none"> Migration Team will be publishing a Migration Troublesome MPANs PPIR. This PPIR will look to ask Suppliers to identify the volume of MPANs they have within their portfolio impacted by this issue. This PPIR will be published on the 16th February alongside a detailed Guidance document to support completion. PPIR deadline is the 13th March. Following completion, Migration Team will produce a risk report that is issued to MWG and MCAG on all Migration Exclusions and Remediations. 		14	14
R1145	There is a risk that achieving proven performance of overall MHHS Design TOM may take longer than anticipated, delaying the overall Migration timeline	<ul style="list-style-type: none"> While new issues may still arise, the immediate risk has been significantly reduced following the fixes implemented by Elexon. The identification of the issue with deappointing DAs in legacy and that discrepancy could be seen in Elexon's reporting, which shows that we have reached sufficient volume of MHHS settled MPANs for any implications for settlement to start to be seen 		14	14
R1221	There is a risk that the right controls (including SLAs) may not be sufficient to support BSCCo Service Management processes, which may be a risk to M15	<ul style="list-style-type: none"> Programme continues to monitor this risk, Elexon have implemented service improvements. Programme expectation is that this will lead to an improvement in containment of service management targets. This risk is linked to Recommendation 4 from the ELS exit recommendations that were shared at TORWG on 04-Feb 		10	14
R1225	There is a risk that an operational issue affects the ability to meet M15	<ul style="list-style-type: none"> Migrations recommenced on 15/01, following the P2 issue with D0209 flows (i266). Remains a risk for M15. Migration numbers are being recovered, probability reduced to 2. Risk to remain open as this could happen again in the future 		11	11
R499	There is a risk that not all MPANs are migrated by M15 due to lack of incentives by Ofgem for PPs to complete migration according to the Migration plan	<ul style="list-style-type: none"> Ofgem decision expected early Feb '26 - Risk score to be reviewed once we have sight of response details 	<ul style="list-style-type: none"> Migrating old MPANs 	10	10


Key	
○	Current Score
●	Previous Score

Programme Updates

INFORMATION: Provide updates from L2/3 governance groups and wider Programme activity

Programme (PMO)

0 mins – to be taken as read and discussed by exception



Governance group updates

Programme Steering Group (PSG)

PSG 04 February 2026

Migration Update: A Migration update outlined Migration progress to date. Migration has restarted since a pause and is recovering progress.

Qualification Update: A Qualification update was provided with wave 1 complete and waves 2 - 4 on track.

Early Life and Hypercare Update: Programme and Elexon provided an overview of ELS Progress and current view on ELS Exit which is planned for 12 February, with both parties supportive of an Exit.

Hypercare systems are progressing well across the Central Parties.

IPA Current Status Update: The IPA provided an update on progress and activities, and are supportive of the planned ELS exit.

Readiness Assessment 7 Update: SRO approved an updated timeline proposed to the next Readiness Assessment 7.

PSG papers available [here](#).

Migration & Cutover Advisory Group (MCAG)

MCAG 18 December 2025

ELS Phase 3 Entry: SRO approved Entry into ELS Phase 3, with no objections raised by MCAG members.

Migration Execution: Programme provided an update on Migration Execution, with Execution and Completion on track.

Migration Exclusion List: An update on Migration Exclusion and Remediation lists was presented and the Programme noted that a PPIR will be shared with all Suppliers in Q1 2026.

MWG update: Programme gave an overview of most recent MWG meeting.

MCAG papers available [here](#).

Qualification Advisory Group (QAG)

QAG 28 January 2026

Programme Milestones Related to QAG: T3 milestones related to Wave 1 Final QAD submission, Wave 1 Execution End, and Wave 3 Execution start were approved.

Qualification Planning: 55 PPIRs have been submitted, remaining Participants were encouraged to submit.

L3/L4 Validation: All PPs were asked to address validation issues as soon as possible with guidance to support this expected to be published soon.

QAG papers available [here](#)

Wider Programme Updates

Participant Checklist:

This week's Participant Checklist includes the following items for Programme participant review, feedback and awareness:

1. REMINDER: Timelines for upcoming Qualification activities by Wave - **please note the various deadlines for the Wave you're in**
 - The deadline for all **Wave 4 participants** to complete **Smoke Testing** is **Thursday 26 February 2026**
2. NEW! Migration Update
3. NEW! Participant Lessons Learned Central Repository published
4. NEW! Uplifted Non-Systems Integration Testing (SIT) participant Qualification Journeys and Qualification Approach & Plan (QA&P) Plans on a Page (PoaPs)

You can view the **Participant Checklist** on the respective **Planning pages** of the [Collaboration Base](#) and the [MHHS website](#). In the Participant Checklist you can view upcoming consultations and key deliverables, as well as the latest status of Change Requests in the **Master Change Request Dashboard** tab.

Upcoming Governance Meetings:

Here's what's coming up over the next week:

- **Wednesday 11 February 2026:** [Transition & Operational Readiness Working Group \(TORWG\)](#) at 14:00
- **Thursday 12 February 2026:** [Migration & Cutover Advisory Group \(MCAG\)](#) at 10:00
- **Thursday 12 February 2026:** [Migration Working Group \(MWG\)](#) at 14:00
- **Wednesday 18 February 2026:** [Qualification Advisory Group \(QAG\)](#) at 10:00
- **Wednesday 18 February 2026:** [TORWG](#) at 14:00
- **Thursday 19 February 2026:** [Settlement Timetable Expert Group \(STEG\)](#) at 14:00

Working Group Progress Report

Migration and Cutover Advisory Group (MCAG)			
	Migration Working Group (MWG)	Transition & Operational Readiness Working Group (TORWG)	Settlement Timetable Expert Group (STEG)
Upcoming meeting's agenda items	12 February 2026 <ul style="list-style-type: none"> • Summary of Migration Execution • Sprint Planning • Migration Observations and Lessons Learnt • Migration Exclusions • Qualification Planning – PPIR Update • MWG Backlog • Top Programme Risks related to MWG • Programme Updates 	Last TORWG was 11 February 2026	19 February 2026 <ul style="list-style-type: none"> • TBC
Agenda items from last meeting	15 January 2026 <ul style="list-style-type: none"> • 2026 Look Ahead • Summary of Migration Execution • Sprint 1 Planning • Migration Exclusions • PPIR – Impact of Updated End-to-End Journey Map • Migration Observations and Lessons Learnt • MWG Backlog • Top Programme Risks related to MWG • Programme Updates 	11 February 2026 <ul style="list-style-type: none"> • Early Life Support Model and Process • Industry Reporting Set out within the ELS Model <ul style="list-style-type: none"> ○ Elexon Service Management Reporting ○ Settlement Reporting ○ Migration Process Reporting ○ DIP Monitoring • Risks or Issues Raised by Industry <ul style="list-style-type: none"> ○ Issues raised by RECCo ○ Issues raised by Participants 	06 February 2026 <ul style="list-style-type: none"> • Introduction • Plan • Governance Structure • Settlement Monitoring & Criteria • Migration Reporting & Criteria • M16 Risks


Qualification Advisory Group (QAG)	
	Qualification and E2E Sandbox Working Group (QWG)
Upcoming meeting's agenda items	10 March 2026 <ul style="list-style-type: none"> • TBC
Agenda items from last meeting	10 February 2026 <ul style="list-style-type: none"> • Qualification Wave Update • Qualification Progress Update • DIP Onboarding Update • L3/L4 Validation • QT Update • PIT Completion Reminder • Sandbox Testing • Wave 4 Readiness • QA&P Update • PPIR Update • Independent Programme Assurance • QT Artefacts • Qualification RAID review

Summary and Next Steps

INFORMATION: Summarise actions/decisions and look ahead to the next MCAG

Chair & Secretariat

5 mins



Summary and Next Steps

Next steps:

1. Confirm actions and decisions from meeting
 2. Date of next MCAG: **24 March 2026 at 2pm**
-
1. Dates of next working groups:
 - Date of next STEG: **27 February 2026 at 2pm**
 - Date of next MWG: **12 February 2026 at 2pm**

Upcoming agenda items:

Meeting dates	24 March 2026
Relevant milestones or activities	
Agenda items	<ul style="list-style-type: none">• Summary of Migration Execution• Summary of Migration Dependencies• Migration Exclusion List
Standing items	<ul style="list-style-type: none">• MWG Update• Programme Milestones related to MCAG• Top Programme Risks related to MCAG• Programme Updates• STEG Update
