



**MHHS
PROGRAMME**
Industry-led, Elexon facilitated

Extraordinary Migration and Cutover Advisory Group (eMCAG) #26.1 – 07 July 2026

Version 1.0

MHHS-DEL4566

Agenda


#	Item	Objective	Type	Lead	Time	Page
1	Welcome	Agenda and Chair Welcome	Information	Chair	14:30-14:35 5 mins	2
2	Decision Criteria and Process for the Settlement Timetable	Decision to approve the agreed decision criteria and associated decision process for the settlement timetable.	Decision	Programme	14:35-15:15 40 mins	3
3	Programme Milestone Updates	Overview and approval of updates to upcoming Programme Milestones related to MCAG	Information/ Decision	Programme	15:15-15:25 10 mins	5
4	Summary and Next Steps	Summarise actions/decisions and look ahead to the next MCAG	Information	Chair and Secretariat	15:15-15:20 5 mins	7

Decision Criteria and Process for the Settlement Timetable

DECISION: Decision to approve the agreed decision criteria and associated decision process for the settlement timetable.

Programme

40 mins

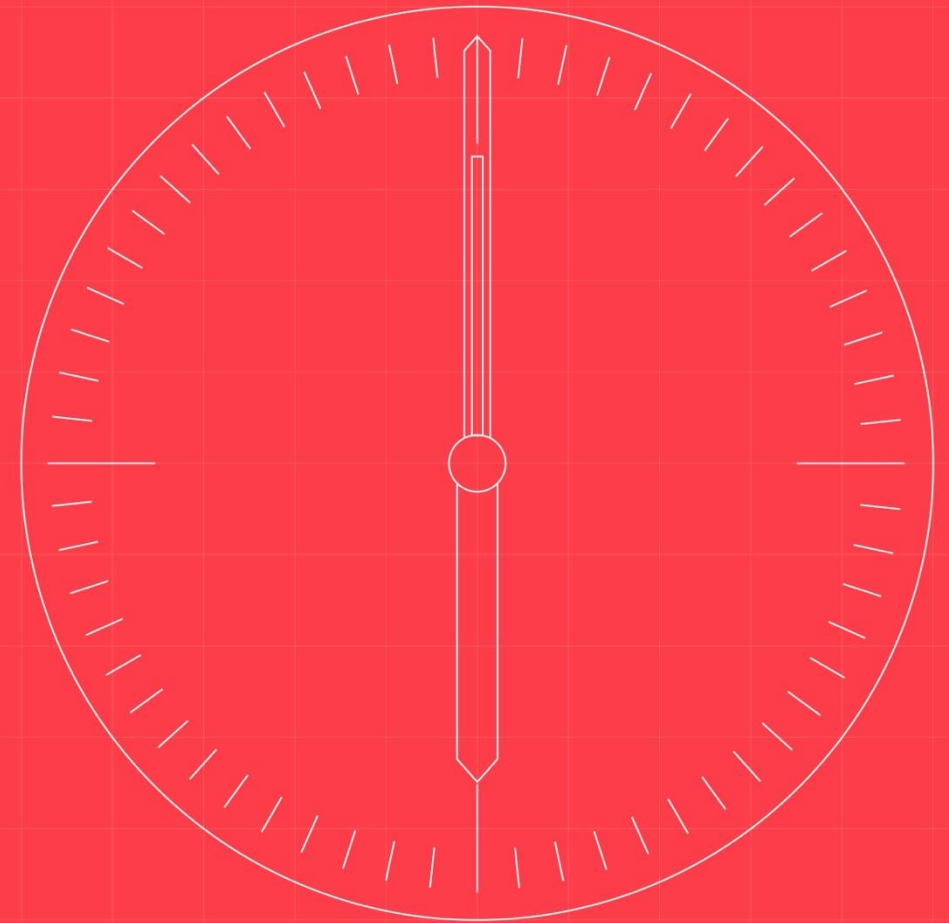

Decision Criteria – RF Changes to 7 & 4 Months

Introduction

- STEG has been considering the criteria that would enable the decision to be taken to Shorten the RF timing to 7 and 4 months
- Criteria were developed by STEG and a consultation with industry undertaken.
- The Results of the consultation and comment themes were provided to MCAG on [23 June 2026](#).
- Responses to the comment themes and updated Decision Criteria were provided and subsequently discussed in STEG on [24 June 2026](#).
- Following discussion STEG [agreed to make a recommendation to MCAG](#) to approve and baseline these acceptance criteria.
- An artefact detailing the agree criteria has been created for change control purposes, available in the [MCAG area of the Collaboration Base](#).

DECISION


eMCAG **approves** RF Decision Criteria recommended by STEG as detailed in MHHS-DEL4564 Updated M16 Decision Criteria v1.0

Programme Milestone Updates

DECISION: Overview and approval of updates to upcoming Programme Milestones related to MCAG

Programme

10 mins

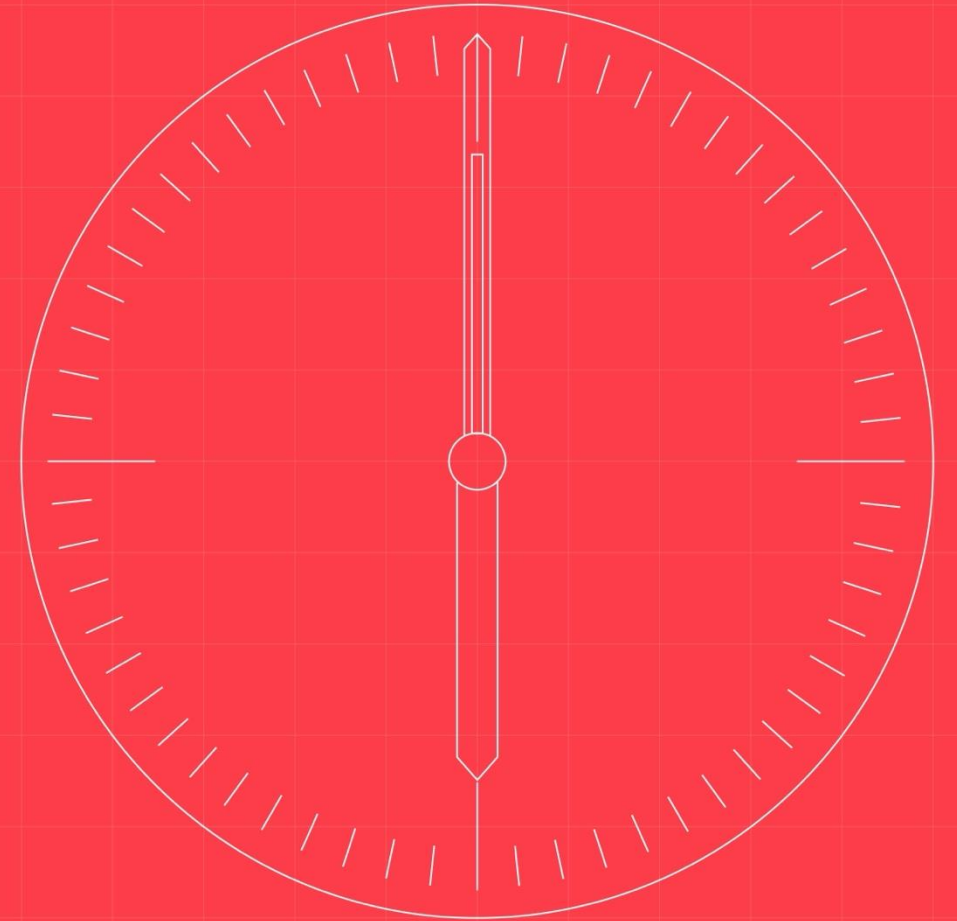

M16 Plan Update: Milestone Changes for Approval – eMCAG Review

Following agreement of the M16 decision criteria, the Programme has refined a small number of milestones to align the plan with the latest Consultation inputs, STEG activity and confirmed governance dates. The intended outcomes remain unchanged.

- **T3-MI-0500 ‘M16 Approach Approved at eMCAG’:** Updated to reflect eMCAG approval on **07/07/26**, allowing time to address issues raised through the initial Consultation.
- **T2-MR-0500 ‘MCAG endorses STEG Assessment that M16 likely to be met’:** Updated to **25/08/26** to align with the regular August MCAG, following initial Consultation analysis and removing the need for an additional eMCAG.
- **T2-RA-0700 ‘Readiness Assessment 8 Complete’:** Updated following STEG on **25/06/26**. Readiness Assessment 8 (RA8) has been decoupled from the M16 decision choreography, brought forward to start on **01/07/26**, and will complete on **02/09/26**, allowing time for detailed analysis, participant deep dives and reduced availability during the summer leave period.
- **T2-EL-0200 ‘eMCAG Approve Recommendation to Change to RF 7 Months Calendar’:** Updated to **15/09/26** to align with planned eMCAG.


DECISION	eMCAG approves the update to Milestone ‘ T3-MI-0500 M16 Approach Approved at eMCAG ’, with the approval date moved from 23/06/26 to 07/07/26 .
DECISION	eMCAG approves the update to Milestone ‘ T2-MR-0500 MCAG endorses STEG Assessment that M16 likely to be met ’, with the milestone date moved to 25/08/26 .
DECISION	eMCAG approves the update to Milestone ‘ T2-RA-0700 Readiness Assessment 8 Complete ’, with the assessment starting on 01/07/26 and completing on 02/09/26 .
DECISION	eMCAG approves the update to Milestone ‘ T2-EL-0200 eMCAG Approve Recommendation to Change to RF 7 Months Calendar ’, with the milestone date moved from 18/09/26 to 15/09/26 .

Summary and Next Steps

INFORMATION: Summarise actions/decisions and look ahead to the next MCAG

Chair & Secretariat

5 mins

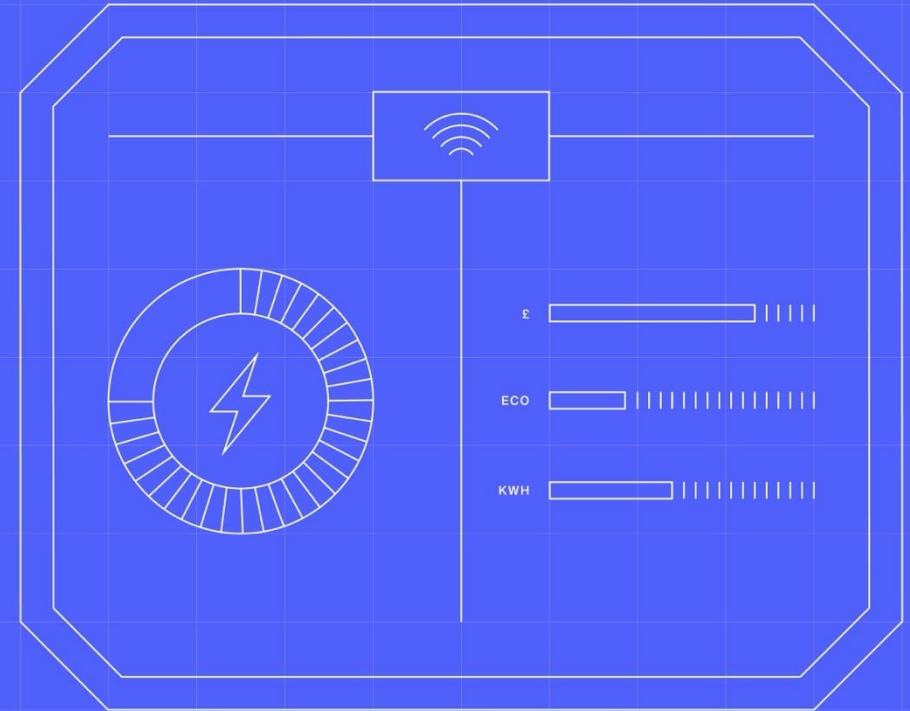

Summary and Next Steps

Next steps:

- 1. Confirm actions and decisions from meeting
- 2. Date of next MCAG: **28 July 2026 at 2pm**

Dates of next working groups:

- Date of next STEG: **08 July 2026 at 2pm**
- Date of next MWG: **09 July 2026 at 2pm**

Upcoming agenda items:

Meeting dates		28 July 2026
Relevant milestones or activities	• N/A	
Agenda items	• Summary of Migration Execution • Summary of Migration Dependencies • Migration Exclusion List • MWG Update • STEG Update	
Standing items	• Programme Milestones related to MCAG • Top Programme Risks related to MCAG • Programme Updates	
