



**MHHS
PROGRAMME**
Industry-led, Elexon facilitated

MHHS Change Control Webinar #11

CR061- 06 May 2025

Version 1.0

MHHS-DEL3692


Document Classification: Public

Agenda

#	Item	Objective	Lead	Time	Page
1	Welcome		MHHS PMO	14.00 - 14.05 5 mins	1
2	Presentation of CR061	Alignment of M10 (go live) delivery date to 22.09.25 for clarification	Matthew Breen, MHHS Programme	14.05 – 14.20 15 mins	3
3	CR061 Q&A		All	14.20 – 14.30 10 mins	5

Presentation of CR061

Matthew Breen, MHHS Programme
15 mins

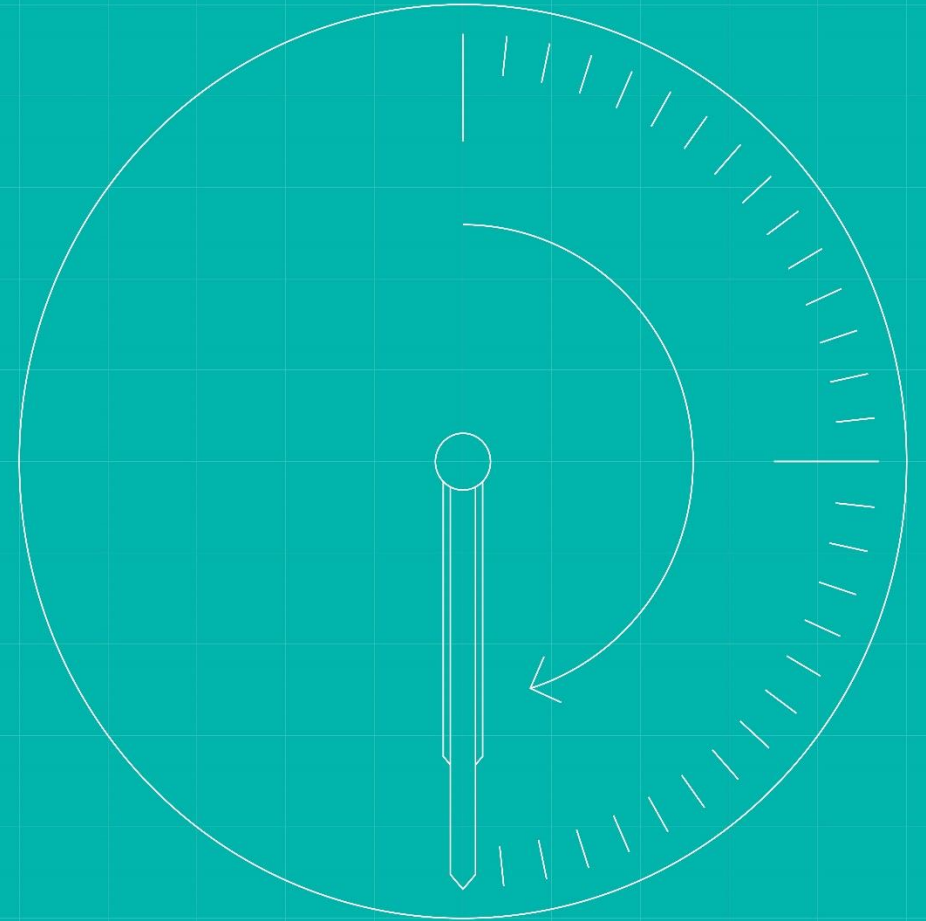

Alignment of M10 (go live) delivery date to 22.09.25 for clarification

Issue Statement:

- As per CR055, the M10 milestone date was set to 24/09/25. The Programme have always set M10 to be two days following Systems go live, following the baselined M10/M11 Cutover Plan, to allow time for evidence to be gathered for a Governance approval after the event, to ensure appropriate approval of M10 achievement at PSG.
- Whilst this approach has been communicated in the M10/M11 Cutover Plan and industry forums, there has been some confusion among Programme Participants as to when systems go live.

Description of Change:

- It is proposed that the M10 milestone is moved two days forward from 24/09/25 to 22/09/25 to align with when Central Systems go live at M8 for the avoidance of doubt.
- This will have no impact on the requirements of industry participants but will provide additional clarity as to when the Central Systems go live.
- The Programme will add an additional milestone to 24/09/25 to reflect the completion of the Governance approval.

Target Date of Change and Next Steps:

- Alignment of M10 (go live) delivery date as soon as possible.
- Upon the completion of the industry Impact Assessment, a recommendation will be made by the Change Board to approve or reject the proposed change.

**MHHS
PROGRAMME**
Industry-led, Government facilitated

Change Request Form

Change Request details

Change Request details			
Change Request Title	Alignment of M10 (Go live) delivery date to 22.09.25 for clarification		
Change Request Number	CR061		
Originating Advisory / Working Group	Various		
Risk/Issue reference			
Change Raiser	Matthew Green, MHHS Programme	Date raised:	06/05/25

For further guidance on how to complete this document please see the supporting Change Request Form Guidance for Programme Participants. The guidance will support raising a change and responding to a change request via Impact Assessment. The Change Raiser should consider sharing the draft Change Request Form with impacted programme parties, prior to submission to PMO. The guidance, as well as other key documents are referenced below and can be found via the MHHS website.

Change Request to be read in conjunction with:

MHHS Change Request Form Guidance for Programme Participants
MHHS Change Control Approach
MHHS Governance Framework
Ofgem's MHHS Transition Timetable


© Elsevier Limited 2024

**MHHS
PROGRAMME**

MHHS-DEL3686 CR061 Draft

CR061 Q&A

*All
10 mins*

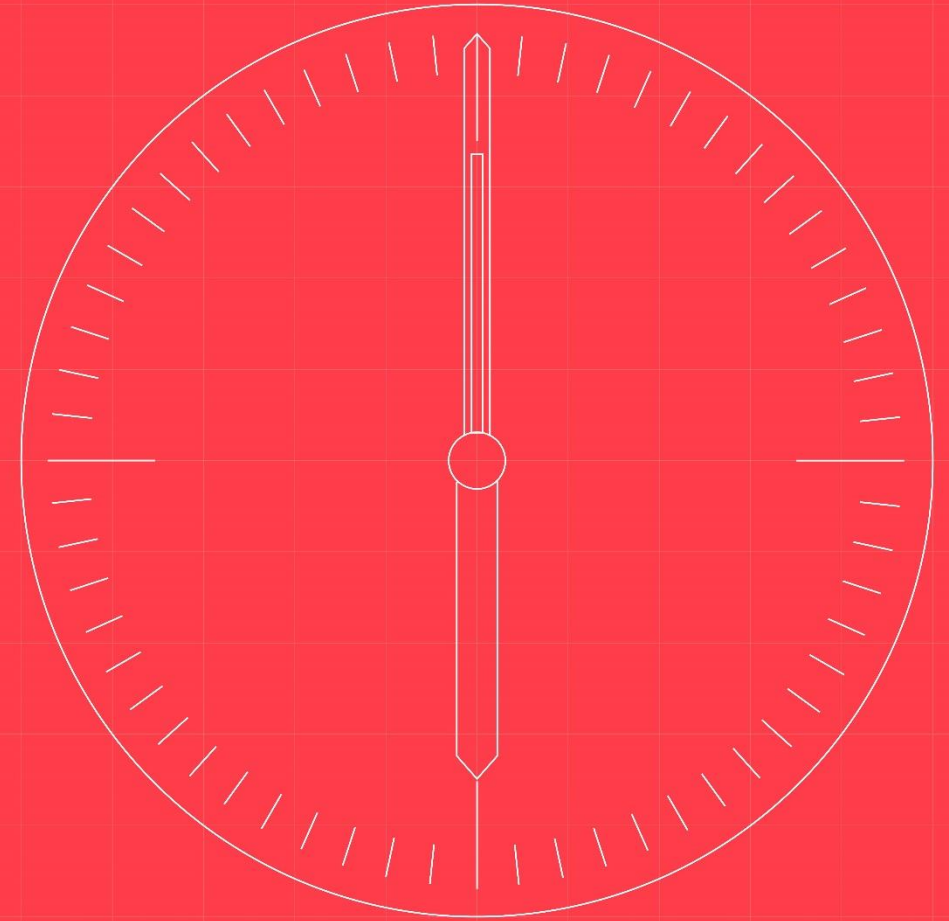

Thank you
